


PLAN VIEW OF WALL FOOTING


ESTIMATED DOWEL BAR QUANTITY

\_\_\_\_\_ LIN. FT. OF WALL FOOTING = \_\_\_\_\_ DOWEL BARS

\_\_\_\_\_ DOWEL BAR SPACING

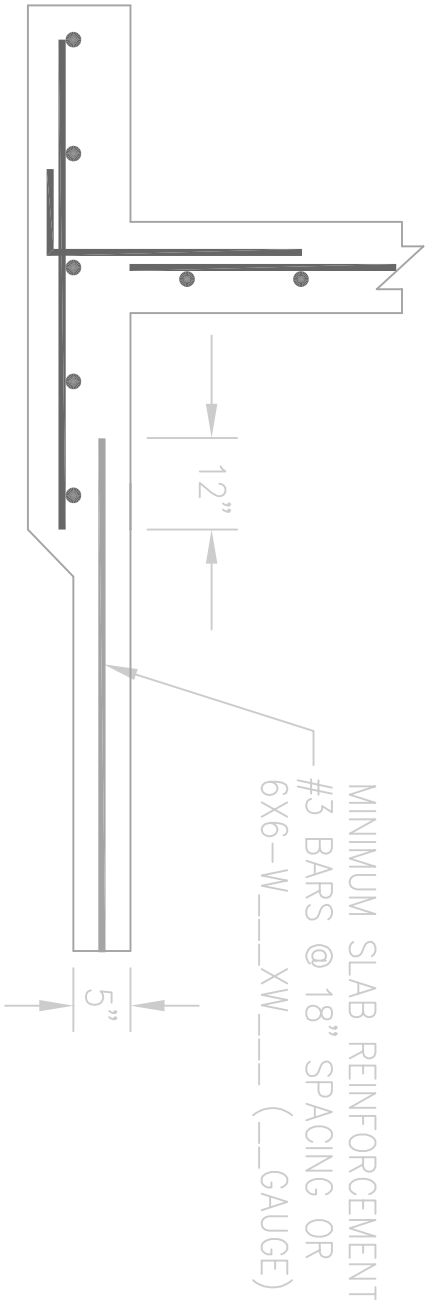

WALL FOOTING AND FLOOR SLAB POURED TOGETHER

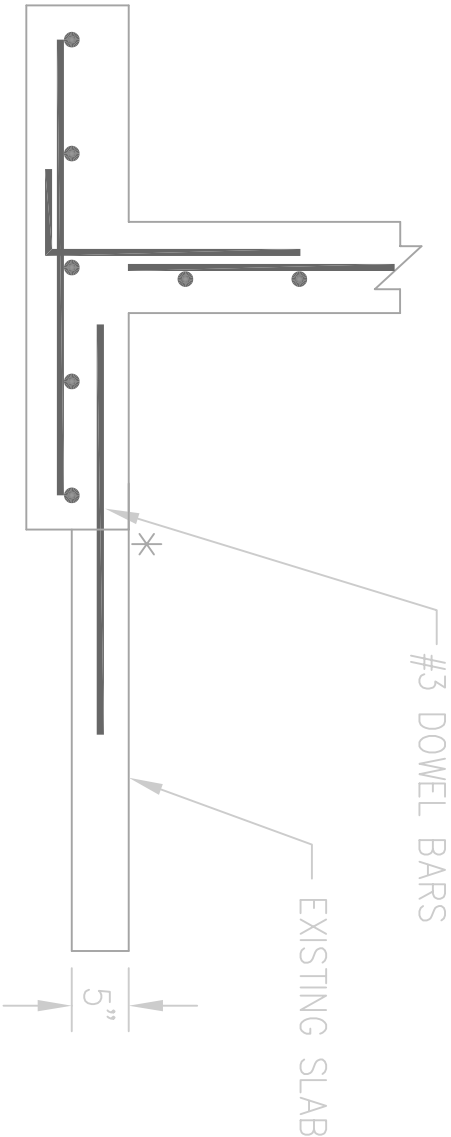

#3 DOWEL BARS – LENGTH 3'-0"  
EMBED 18" INTO WALL FOOTING.

WALL FOOTING AND FLOOR SLAB POURED SEPARATELY

\* – SEE PA004 FOR JOINT DETAILS

(ADAPTED FROM WI-570, APRIL 2005)



\_\_\_\_\_ COUNTY, PENNSYLVANIA

RESTRAINING SLAB OPTIONS

Date \_\_\_\_\_

06/23/05

Designed \_\_\_\_\_

Drawn TJA

Checked \_\_\_\_\_

Approved by \_\_\_\_\_

File No. PA-024.dwg

Drawing No. 07/06/07 12:55

PA-024

Sheet \_\_\_\_\_ of \_\_\_\_\_
